

ID	Task Name	Start	Finish	Duration	Oct 14, '18	Oct 21, '18	Oct 28, '18	Nov 4, '18	Nov 11, '18
1	PRDE	Fri 10/12/18	Mon 3/4/19	102 days					
2	PRDE RFP Evaluation and Award	Fri 10/12/18	Mon 11/12/18	22 days					
3	Vendor RFP Submittal	Fri 10/12/18	Fri 10/12/18	1 day					
4	PRDE RFP Response and Vendor Evaluation	Mon 10/15/18	Fri 11/9/18	20 days					
5	PO/Contract Award	Mon 11/12/18	Mon 11/12/18	1 day					
6	PRDE OS and Applications Image	Tue 11/13/18	Wed 11/21/18	7 days					
7	Provide PRDE Laptop for Image Creation	Tue 11/13/18	Tue 11/13/18	1 day					
8	PRDE Image Creation and Verification	Wed 11/14/18	Tue 11/20/18	5 days					
9	Receive Laptop from PRDE with Final Approved Im	Wed 11/21/18	Wed 11/21/18	1 day					
10	SESCO Equipment Acquisition	Thu 11/22/18	Mon 2/18/19	63 days					
11	Ordering	Thu 11/22/18	Thu 2/14/19	61 days					
12	Order Equipment from Manufacturer	Thu 11/22/18	Thu 11/22/18	1 day					
13	Equipment Manufacturing, Etching and Imaging	Fri 11/23/18	Thu 2/14/19	60 days					
14	PRDE Delivery (Warehouse)	Mon 1/21/19	Mon 2/18/19	21 days					
15	1st Equipment Shipment Delivery	Mon 1/21/19	Mon 1/21/19	1 day					
16	2nd Equipment Shipment Delivery	Mon 1/28/19	Mon 1/28/19	1 day					
17	3rd Equipment Shipment Delivery	Mon 2/4/19	Mon 2/4/19	1 day					
18	4th Equipment Shipment Delivery	Mon 2/11/19	Mon 2/11/19	1 day					
19	5th Equipment Shipment Delivery	Mon 2/18/19	Mon 2/18/19	1 day					
20	PRDE Tagging and Inventory System Integration	Tue 1/22/19	Fri 2/22/19	24 days					
21	1st Equipment Shipment Tagging and School Designation	Tue 1/22/19	Fri 1/25/19	4 days					
22	2nd Equipment Shipment Tagging and School Designation	Tue 1/29/19	Fri 2/1/19	4 days					
23	3rd Equipment Shipment Tagging and School Designation	Tue 2/5/19	Fri 2/8/19	4 days					
24	4th Equipment Shipment Tagging and School Designation	Tue 2/12/19	Fri 2/15/19	4 days					
25	5th Equipment Shipment Tagging and School Designation	Tue 2/19/19	Fri 2/22/19	4 days					
26	Pickup and School Delivery	Mon 1/28/19	Fri 3/1/19	25 days					
27	1st Equipment Shipment School Delivery	Mon 1/28/19	Fri 2/1/19	5 days					
28	2nd Equipment Shipment School Delivery	Mon 2/4/19	Fri 2/8/19	5 days					
29	3rd Equipment Shipment School Delivery	Mon 2/11/19	Fri 2/15/19	5 days					
30	4th Equipment Shipment School Delivery	Mon 2/18/19	Fri 2/22/19	5 days					
31	5th Equipment Shipment School Delivery	Mon 2/25/19	Fri 3/1/19	5 days					
32	Invoicing	Tue 1/22/19	Mon 3/4/19	30 days					
33	Warehouse Delivery Completed	Tue 1/22/19	Tue 2/19/19	21 days					
34	1st Equipment Shipment Invoice	Tue 1/22/19	Tue 1/22/19	1 day					
35	2nd Equipment Shipment Invoice	Tue 1/29/19	Tue 1/29/19	1 day					

Project: Doctor's Carolina VoIP Pr
 Date: Fri 10/5/18


Task Summary
 Split Milestone Summary

Project Summary
 External Tasks
 External Milestone
 Inactive Task

Inactive Milestone
 Inactive Summary
 Manual Task
 Duration-only

Manual Summary Rollup
 Manual Summary
 Start-only
 Finish-only

Deadline
 Progress
 Manual Progress

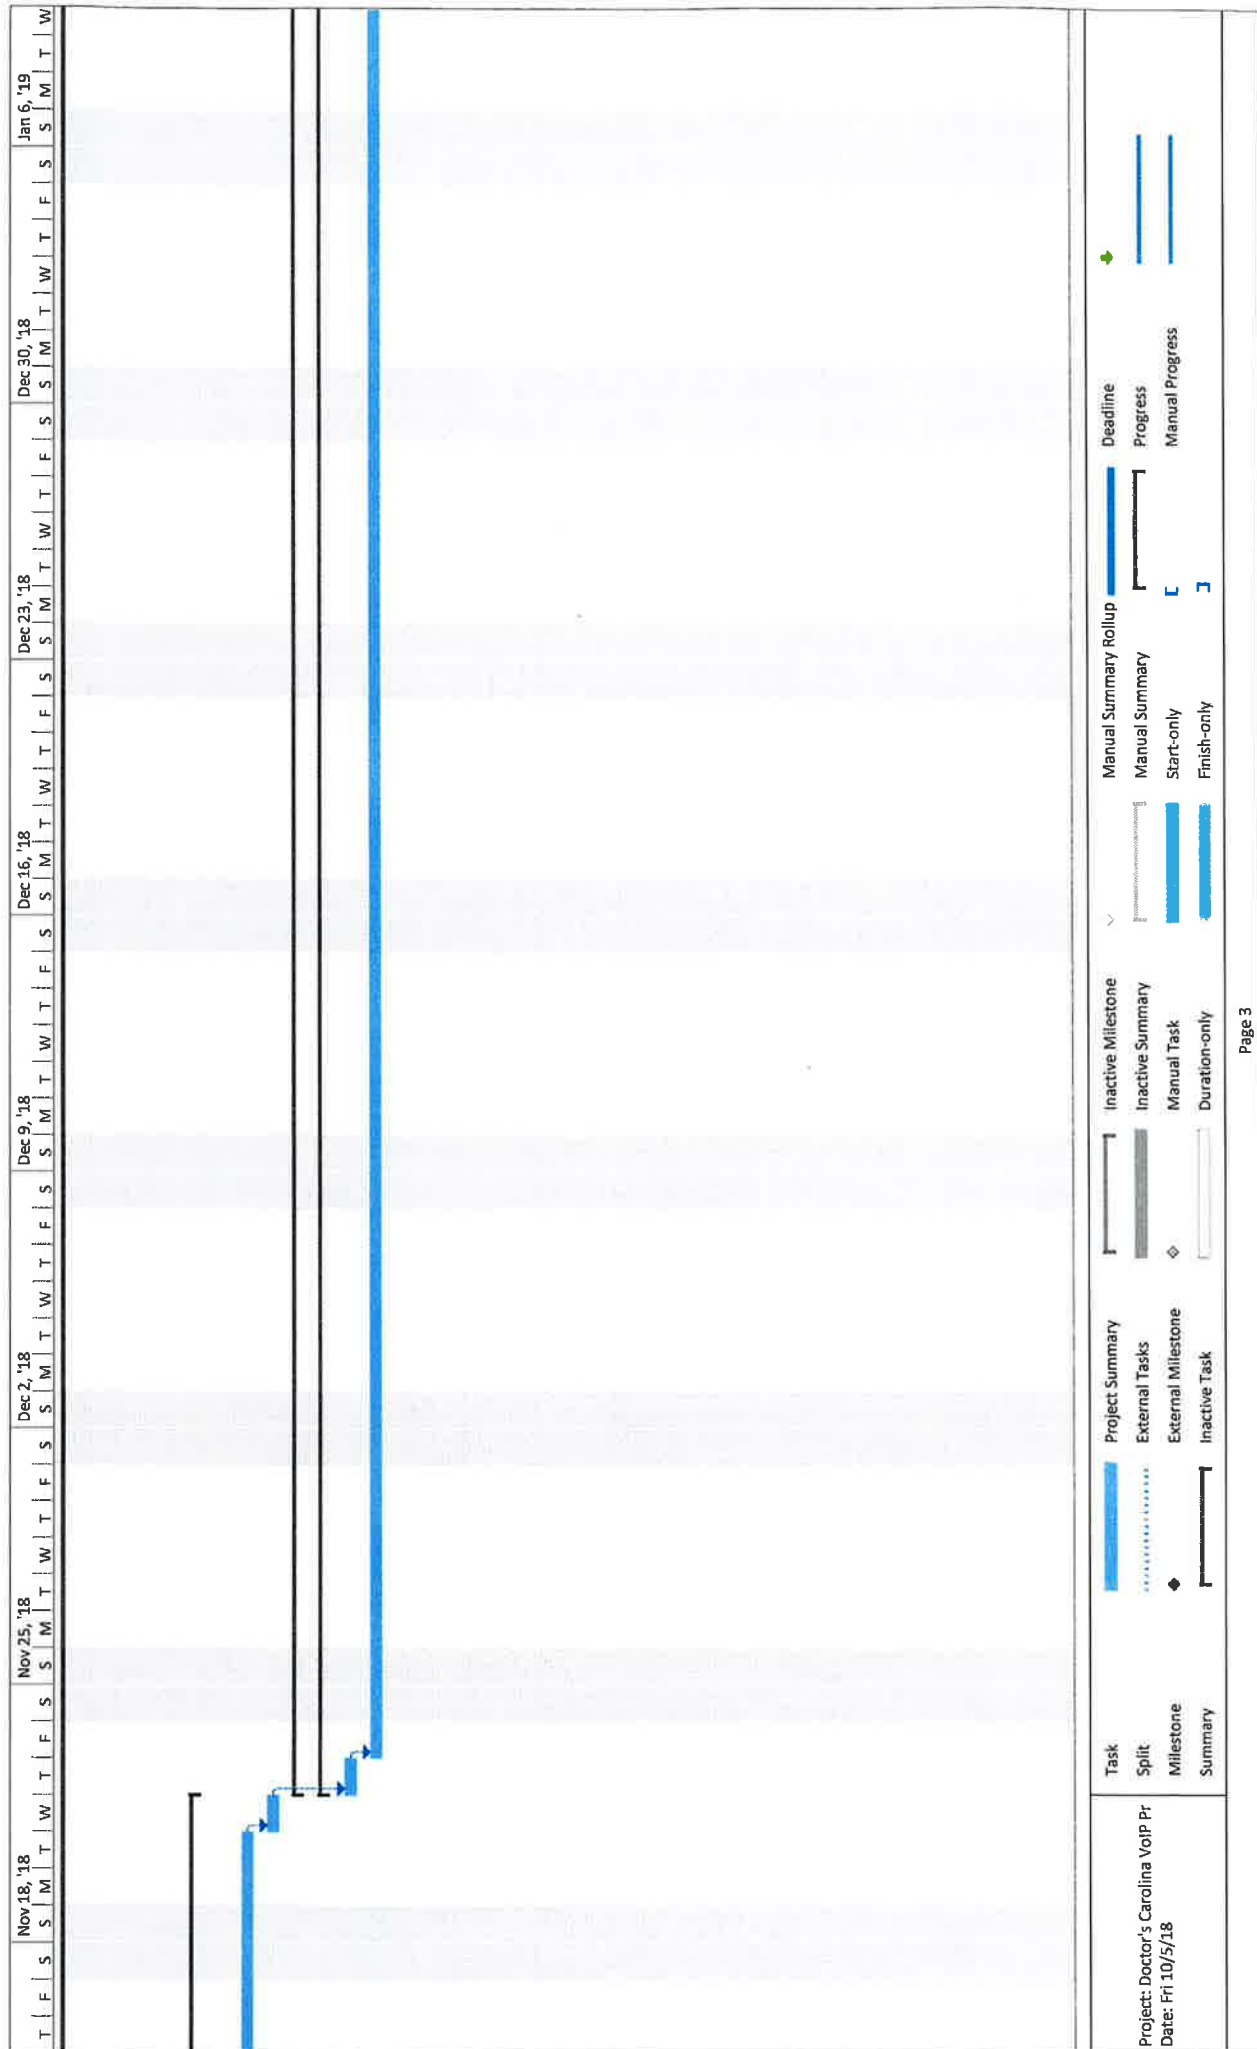

Project: Doctor's Carolina VoIP Pr
 Date: Fri 10/5/18

Task Summary Rollup

- Manual Summary Rollup
- Manual Summary
- Start-only
- Finish-only
- Deadline
- Progress
- Manual Progress


Task Summary

- Project Summary
- External Tasks
- External Milestone
- Inactive Task
- Inactive Milestone
- Inactive Summary
- Manual Task
- Duration-only


Task Summary

- Task
- Split
- Milestone
- Summary

Nov 18, '18	Nov 25, '18	Dec 2, '18	Dec 9, '18	Dec 16, '18	Dec 23, '18	Dec 30, '18	Jan 6, '19
S	S	S	S	S	S	S	S
M	M	M	M	M	M	M	M
T	T	T	T	T	T	T	T
W	W	W	W	W	W	W	W
T	T	T	T	T	T	T	T
F	F	F	F	F	F	F	F
S	S	S	S	S	S	S	S
Task	Project Summary	Inactive Milestone	Inactive Milestone	Manual Summary Rollup	Deadline	Progress	Manual Progress
Split	External Tasks	Inactive Summary	Inactive Summary	Manual Summary	Progress	Progress	Manual Progress
Milestone	External Milestone	Manual Task	Manual Task	Start-only	Manual Progress	Manual Progress	Manual Progress
Summary	Inactive Task	Duration-only	Duration-only	Finish-only	Manual Progress	Manual Progress	Manual Progress

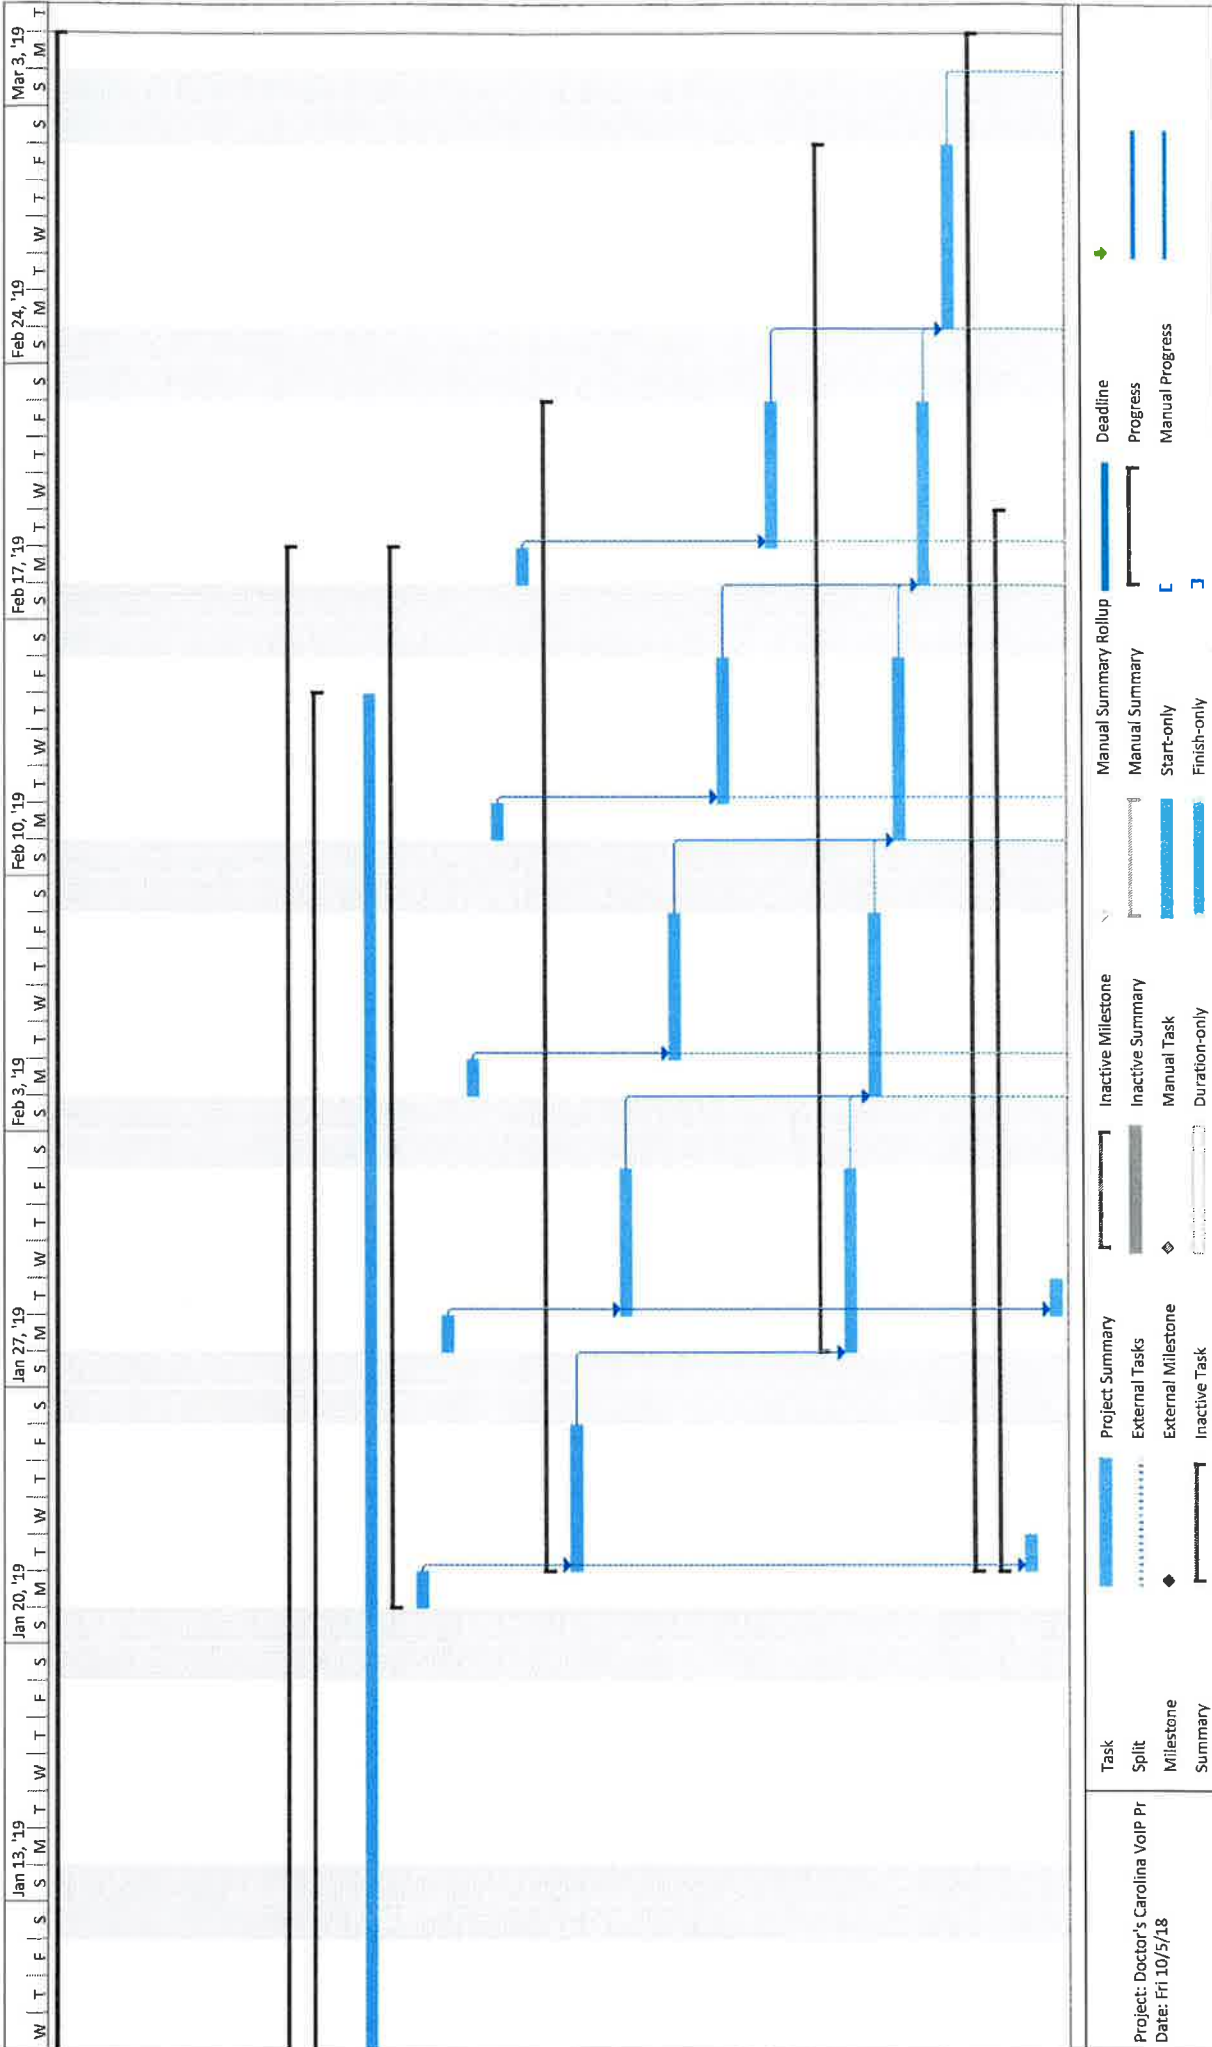

Project: Doctor's Carolina VolP Pr
 Date: Fri 10/5/18

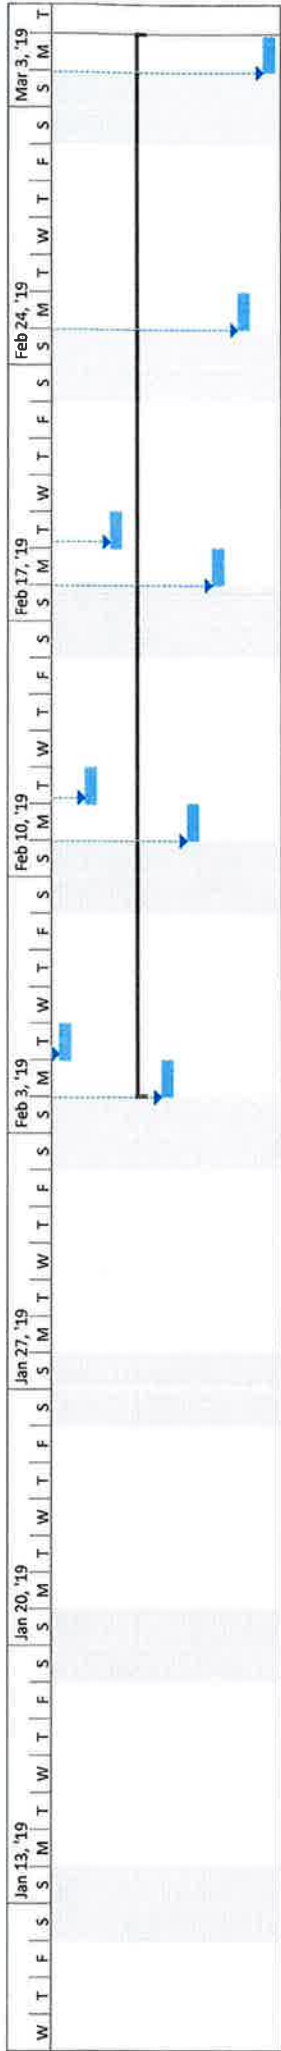

Project: Doctor's Carolina VoIP Pr
Date: Fri 10/5/18

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline
Split	External Tasks	Inactive Summary	Manual Summary	Progress
Milestone	External Milestone	Manual Task	Start-only	Manual Progress
Summary	Inactive Task	Duration-only	Finish-only	
