

ID	Task Name	Start	Finish	Duration	Oct 14, '18							Oct 21, '18							Oct 28, '18							Nov 4, '18							Nov 11, '18						
					S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M
1	PRDE	Fri 10/12/18	Mon 3/4/19	102 days																																			
2	PRDE RFP Evaluation and Award	Fri 10/12/18	Mon 11/12/18	22 days																																			
3	Vendor RFP Submittal	Fri 10/12/18	Fri 10/12/18	1 day																																			
4	PRDE RFP Response and Vendor Evaluation	Mon 10/15/18	Fri 11/9/18	20 days																																			
5	PO/Contract Award	Mon 11/12/18	Mon 11/12/18	1 day																																			
6	PRDE OS and Applications Image	Tue 11/13/18	Wed 11/21/18	7 days																																			
7	Provide PRDE Laptop for Image Creation	Tue 11/13/18	Tue 11/13/18	1 day																																			
8	PRDE Image Creation and Verification	Wed 11/14/18	Tue 11/20/18	5 days																																			
9	Receive Laptop from PRDE with Final Approved im	Wed 11/21/18	Wed 11/21/18	1 day																																			
10	SESCO Equipment Acquisition	Thu 11/22/18	Mon 2/18/19	63 days																																			
11	Ordering	Thu 11/22/18	Thu 2/14/19	61 days																																			
12	Order Equipment from Manufacturer	Thu 11/22/18	Thu 11/22/18	1 day																																			
13	Equipment Manufacturing, Etching and Imaging	Fri 11/23/18	Thu 2/14/19	60 days																																			
14	PRDE Delivery (Warehouse)	Mon 1/21/19	Mon 2/18/19	21 days																																			
15	1st Equipment Shipment Delivery	Mon 1/21/19	Mon 1/21/19	1 day																																			
16	2nd Equipment Shipment Delivery	Mon 1/28/19	Mon 1/28/19	1 day																																			
17	3rd Equipment Shipment Delivery	Mon 2/4/19	Mon 2/4/19	1 day																																			
18	4th Equipment Shipment Delivery	Mon 2/11/19	Mon 2/11/19	1 day																																			
19	5th Equipment Shipment Delivery	Mon 2/18/19	Mon 2/18/19	1 day																																			
20	PRDE Tagging and Inventory System Integration	Tue 1/22/19	Fri 2/22/19	24 days																																			
21	1st Equipment Shipment Tagging and School Designation	Tue 1/22/19	Fri 1/25/19	4 days																																			
22	2nd Equipment Shipment Tagging and School Designation	Tue 1/29/19	Fri 2/1/19	4 days																																			
23	3rd Equipment Shipment Tagging and School Designation	Tue 2/5/19	Fri 2/8/19	4 days																																			
24	4th Equipment Shipment Tagging and School Designation	Tue 2/12/19	Fri 2/15/19	4 days																																			
25	5th Equipment Shipment Tagging and School Designation	Tue 2/19/19	Fri 2/22/19	4 days																																			
26	Pickup and School Delivery	Mon 1/28/19	Fri 3/1/19	25 days																																			
27	1st Equipment Shipment School Delivery	Mon 1/28/19	Fri 2/1/19	5 days																																			
28	2nd Equipment Shipment School Delivery	Mon 2/4/19	Fri 2/8/19	5 days																																			
29	3rd Equipment Shipment School Delivery	Mon 2/11/19	Fri 2/15/19	5 days																																			
30	4th Equipment Shipment School Delivery	Mon 2/18/19	Fri 2/22/19	5 days																																			
31	5th Equipment Shipment School Delivery	Mon 2/25/19	Fri 3/1/19	5 days																																			
32	Invoicing	Tue 1/22/19	Mon 3/4/19	30 days																																			
33	Warehouse Delivery Completed	Tue 1/22/19	Tue 2/19/19	21 days																																			
34	1st Equipment Shipment Invoice	Tue 1/22/19	Tue 1/22/19	1 day																																			
35	2nd Equipment Shipment Invoice	Tue 1/29/19	Tue 1/29/19	1 day																																			

Project: Doctor's Carolina VoIP Pr Date: Fri 10/5/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			


ID	Task Name	Start	Finish	Duration	Oct 14, '18							Oct 21, '18							Oct 28, '18							Nov 4, '18							Nov 11, '18						
					S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
36	3rd Equipment Shipment Invoice	Tue 2/5/19	Tue 2/5/19	1 day																																			
37	4th Equipment Shipment Invoice	Tue 2/12/19	Tue 2/12/19	1 day																																			
38	5th Equipment Shipment Invoice	Tue 2/19/19	Tue 2/19/19	1 day																																			
39	School Delivery Completed	Mon 2/4/19	Mon 3/4/19	21 days																																			
40	1st Equipment Delivery Invoice	Mon 2/4/19	Mon 2/4/19	1 day																																			
41	2nd Equipment Delivery Invoice	Mon 2/11/19	Mon 2/11/19	1 day																																			
42	3rd Equipment Delivery Invoice	Mon 2/18/19	Mon 2/18/19	1 day																																			
43	4th Equipment Delivery Invoice	Mon 2/25/19	Mon 2/25/19	1 day																																			
44	5th Equipment Delivery Invoice	Mon 3/4/19	Mon 3/4/19	1 day																																			

Project: Doctor's Carolina VoIP Pr
Date: Fri 10/5/18

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			




T	F	S	Nov 18, '18	S	M	T	W	T	F	S	Nov 25, '18	S	M	T	W	T	F	S	Dec 2, '18	S	M	T	W	T	F	S	Dec 9, '18	S	M	T	W	T	F	S	Dec 16, '18	S	M	T	W	T	F	S	Dec 23, '18	S	M	T	W	T	F	S	Dec 30, '18	S	M	T	W	T	F	S	Jan 6, '19	S	M	T	W
---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	-------------	---	---	---	---	---	---	---	------------	---	---	---	---

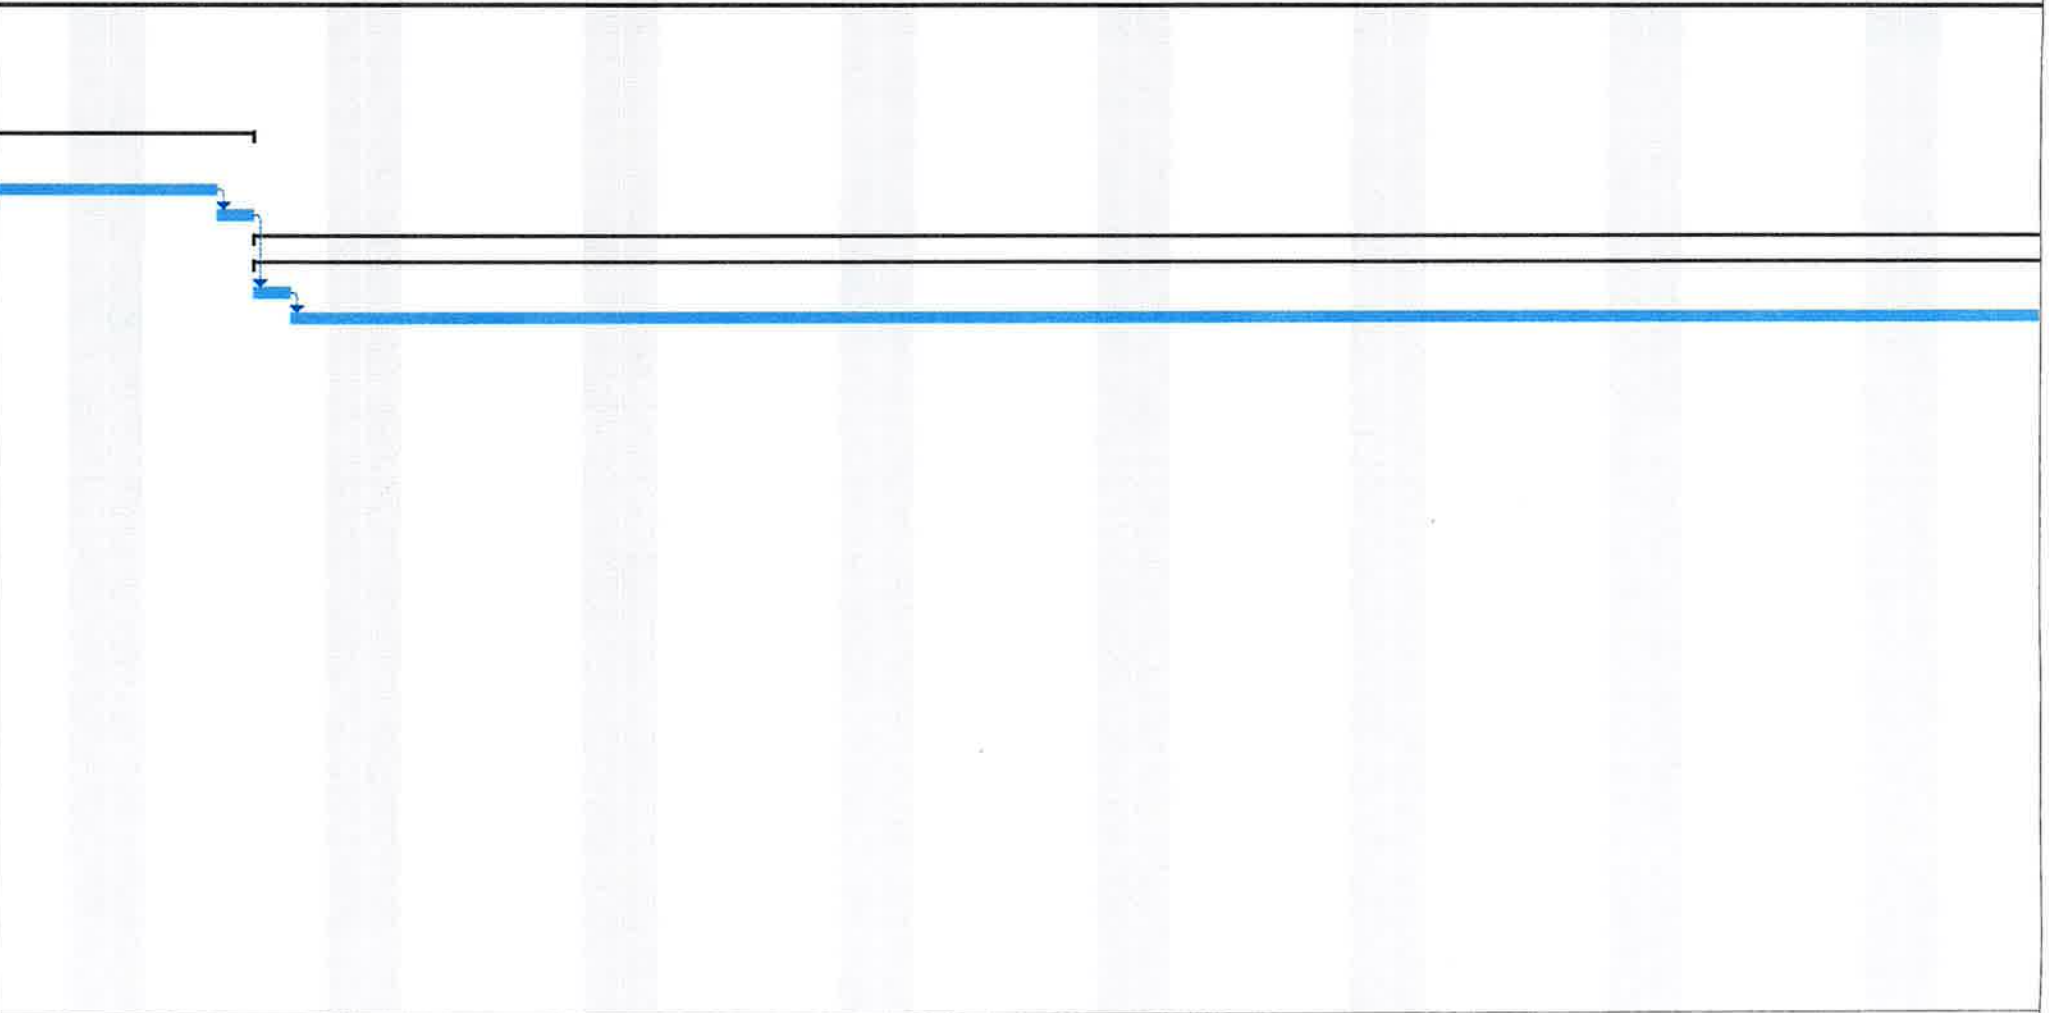


Project: Doctor's Carolina VoIP Pr Date: Fri 10/5/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			

T	F	S	Nov 18, '18							Nov 25, '18							Dec 2, '18							Dec 9, '18							Dec 16, '18							Dec 23, '18							Dec 30, '18							Jan 6, '19						
			S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

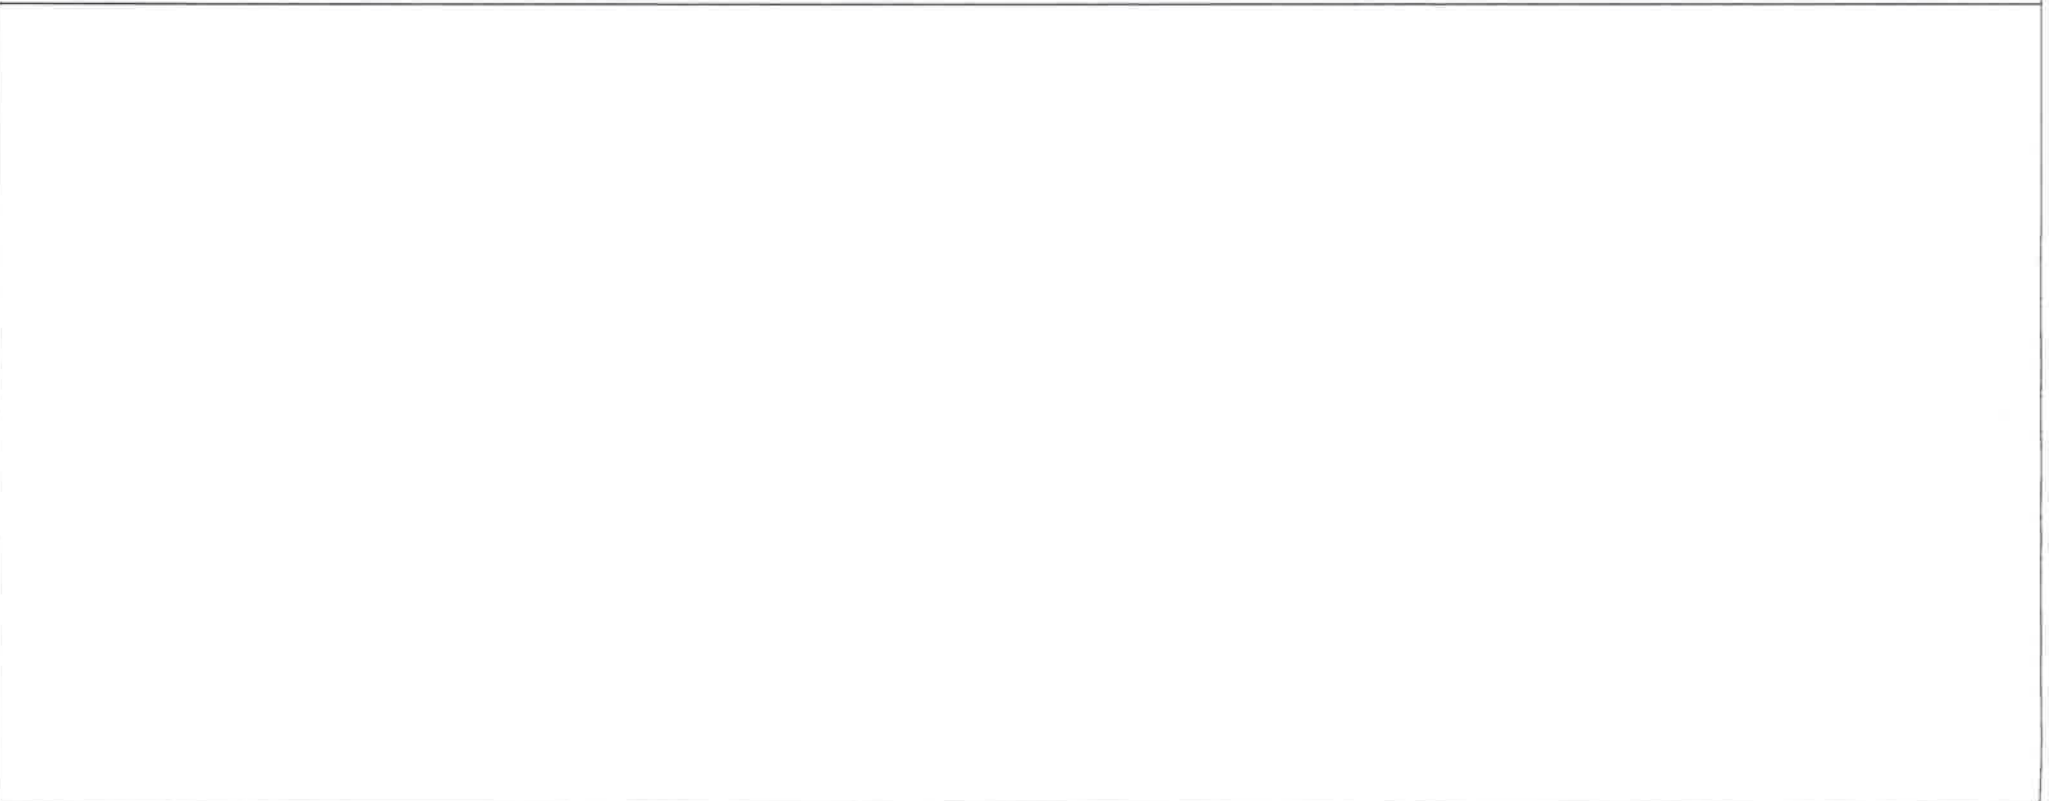


Project: Doctor's Carolina VoIP Pr Date: Fri 10/5/18	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			

Jan 13, '19 Jan 20, '19 Jan 27, '19 Feb 3, '19 Feb 10, '19 Feb 17, '19 Feb 24, '19 Mar 3, '19
 W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T

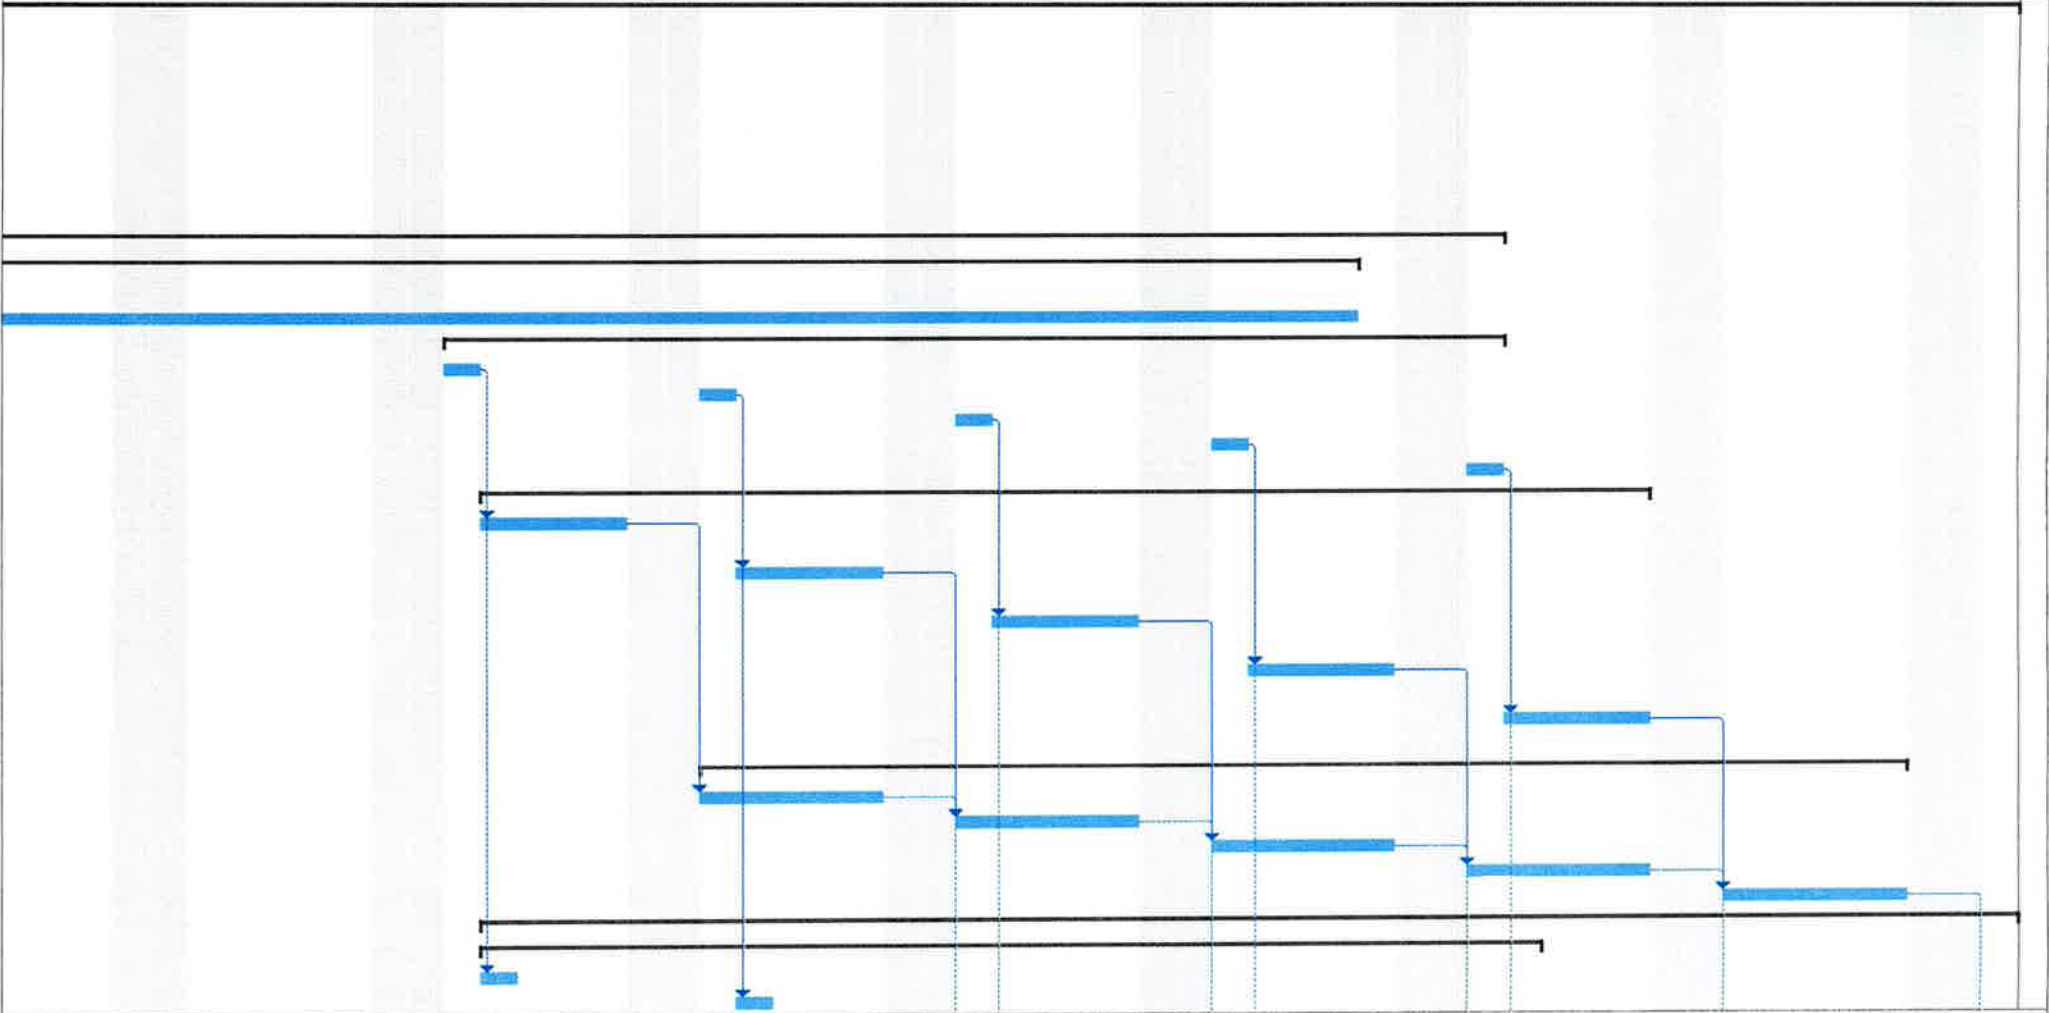

Project: Doctor's Carolina VoIP Pr
 Date: Fri 10/5/18

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline	
Split	External Tasks	Inactive Summary	Manual Summary	Progress	
Milestone	External Milestone	Manual Task	Start-only	Manual Progress	
Summary	Inactive Task	Duration-only	Finish-only		

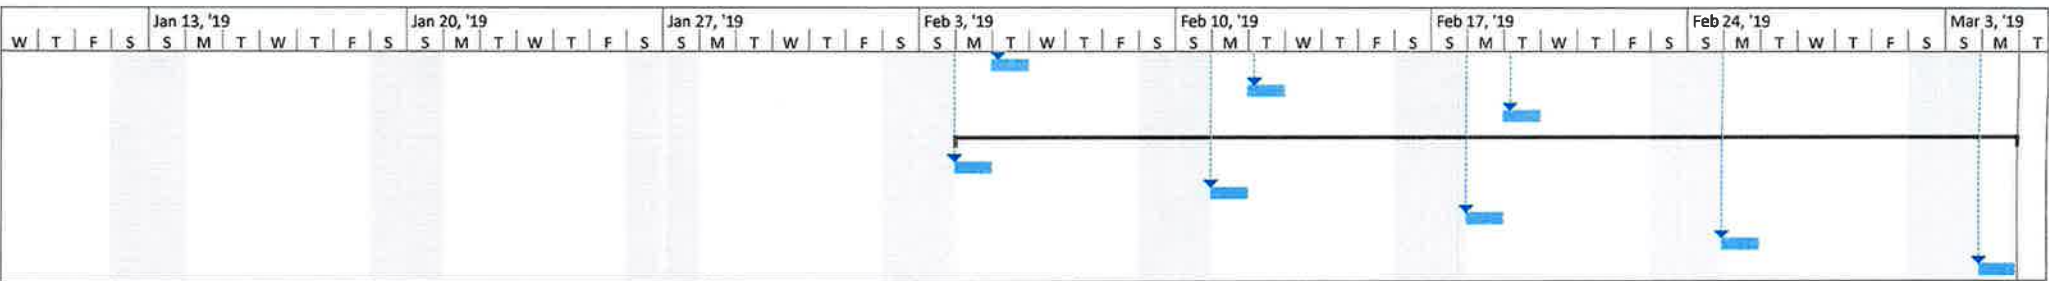

Project: Doctor's Carolina VoIP Pr
Date: Fri 10/5/18

Task		Project Summary		Inactive Milestone		Inactive Summary		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only					
